









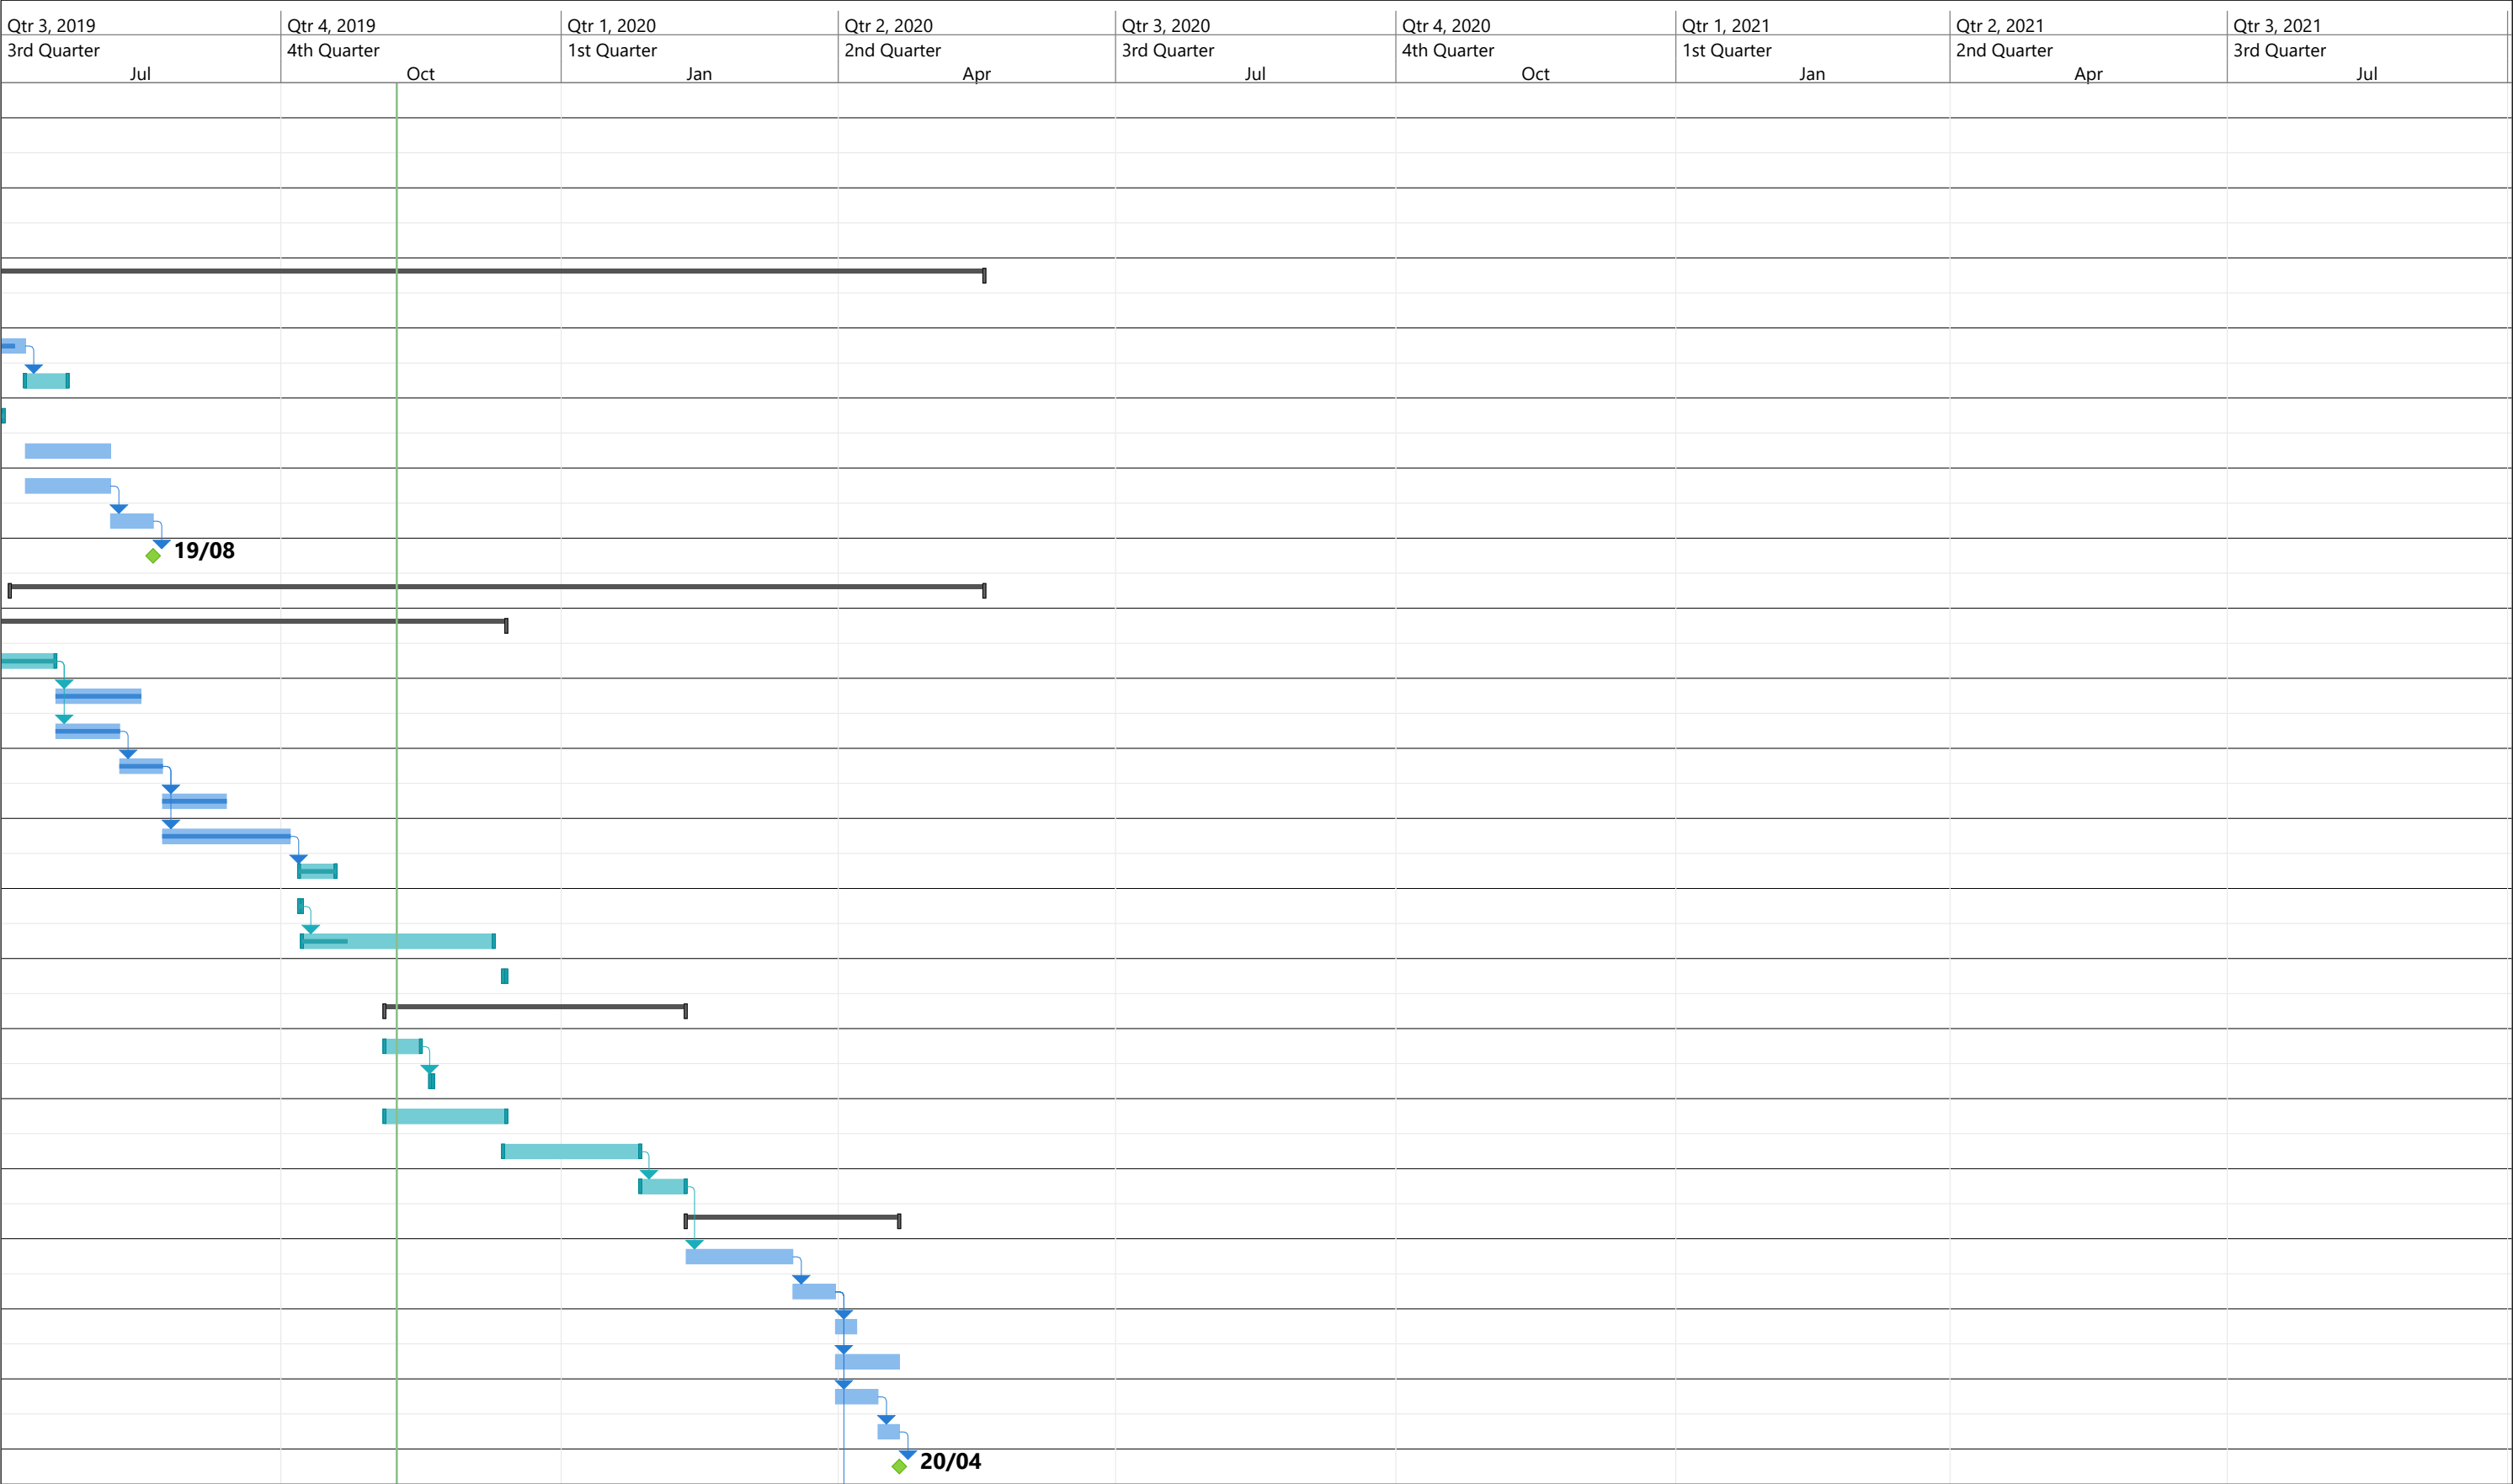












ID	Task Name	Duration	Start	Finish	Qtr 3, 2018	Qtr 4, 2018	Qtr 1, 2019	Qtr 2, 2019	Qtr 3, 2019		
					3rd Quarter	4th Quarter	1st Quarter	2nd Quarter	3rd Quarter		
					Jul	Oct	Jan	Apr	Jul		
1	Liveable Crouch End										
2	1. Inception	34 days	Tue 09/10/18	Fri 23/11/18							
7	2. Pre-engagement	99 days	Sat 13/10/18	Fri 01/03/19							
22	3. Define scope	90 days	Tue 13/11/18	Mon 18/03/19							
27	4. Workshops	90 days	Tue 04/12/18	Mon 08/04/19							
32	5. Concept options (superceded)	290 days	Tue 09/04/19	Mon 18/05/20							
33	Develop concept proposals	9 wks	Tue 09/04/19	Mon 10/06/19							
34	Develop cost plan	4 wks	Tue 11/06/19	Mon 08/07/19							
35	Haringey Review	2 wks	Tue 09/07/19	Mon 22/07/19							
36	Undertake traffic modelling (base) - for G2	8 wks	Tue 07/05/19	Mon 01/07/19							
37	Stage 1 RSA	4 wks	Tue 09/07/19	Mon 05/08/19							
38	Concept Design Feasibility Report	4 wks	Tue 09/07/19	Mon 05/08/19							
39	Client Approval Period	2 wks	Tue 06/08/19	Mon 19/08/19							
40	Client review and approval of feasibility reporting	0 days	Mon 19/08/19	Mon 19/08/19							
41	Consult stakeholders	228 days	Thu 04/07/19	Mon 18/05/20							
49	Testing temporary/trial projects	135 days	Mon 10/06/19	Fri 13/12/19							
50	Trials - scope, cost and options appraisal	29 days	Mon 10/06/19	Thu 18/07/19							
51	Trials Approval from TfL - date tbc	4 wks	Fri 19/07/19	Thu 15/08/19							
52	Haringey Approvals	3 wks	Fri 19/07/19	Thu 08/08/19							
53	Local ward members engagement	2 wks	Fri 09/08/19	Thu 22/08/19							
54	Inform Businesses	3 wks	Fri 23/08/19	Thu 12/09/19							
55	Procure and Implement trials	6 wks	Fri 23/08/19	Thu 03/10/19							
56	Trials and engagement	2 wks	Mon 07/10/19	Fri 18/10/19							
57	Questionniare	1 day	Mon 07/10/19	Mon 07/10/19							
58	Data analysis and questionnaire report	45 days	Tue 08/10/19	Mon 09/12/19							
59	Release results	1 day	Fri 13/12/19	Fri 13/12/19							
60	Questionniare	71 days	Mon 04/11/19	Mon 10/02/20							
61	Draft Questionnaire	10 days	Mon 04/11/19	Fri 15/11/19							
62	Project Board approval	1 day	Tue 19/11/19	Tue 19/11/19							
63	Development of comms	30 days	Mon 04/11/19	Fri 13/12/19							
64	Questionnaire live	32 days	Fri 13/12/19	Sun 26/01/20							
65	Analysis and completion of questionnaire report	11 days	Mon 27/01/20	Mon 10/02/20							
66	6. Concept Proposals - Revisited	50 days	Tue 11/02/20	Mon 20/04/20							
67	Develop concept proposals	5 wks	Tue 11/02/20	Mon 16/03/20							
68	Develop cost plan	2 wks	Tue 17/03/20	Mon 30/03/20							
69	Haringey Review	1 wk	Tue 31/03/20	Mon 06/04/20							
70	Stage 1 RSA	3 wks	Tue 31/03/20	Mon 20/04/20							
71	Concept Design Feasibility Report	2 wks	Tue 31/03/20	Mon 13/04/20							
72	Client Approval Period	1 wk	Tue 14/04/20	Mon 20/04/20							
73	Client review and approval of feasibility reporting	0 days	Mon 20/04/20	Mon 20/04/20							
Project: 20181217 LCE Project_P Date: Fri 08/11/19		Task	<div></div>	Project Summary	<div></div>	Manual Task	<div></div>	Start-only	<div></div>	Deadline	<div></div>
		Split	<div></div>	Inactive Task	<div></div>	Duration-only	<div></div>	Finish-only	<div></div>	Progress	<div></div>
		Milestone	<div></div>	Inactive Milestone	<div></div>	Manual Summary Rollup	<div></div>	External Tasks	<div></div>	Manual Progress	<div></div>
		Summary	<div></div>	Inactive Summary	<div></div>	Manual Summary	<div></div>	External Milestone	<div></div>		
Page 1											



Project: 20181217 LCE Project_P Date: Fri 08/11/19	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

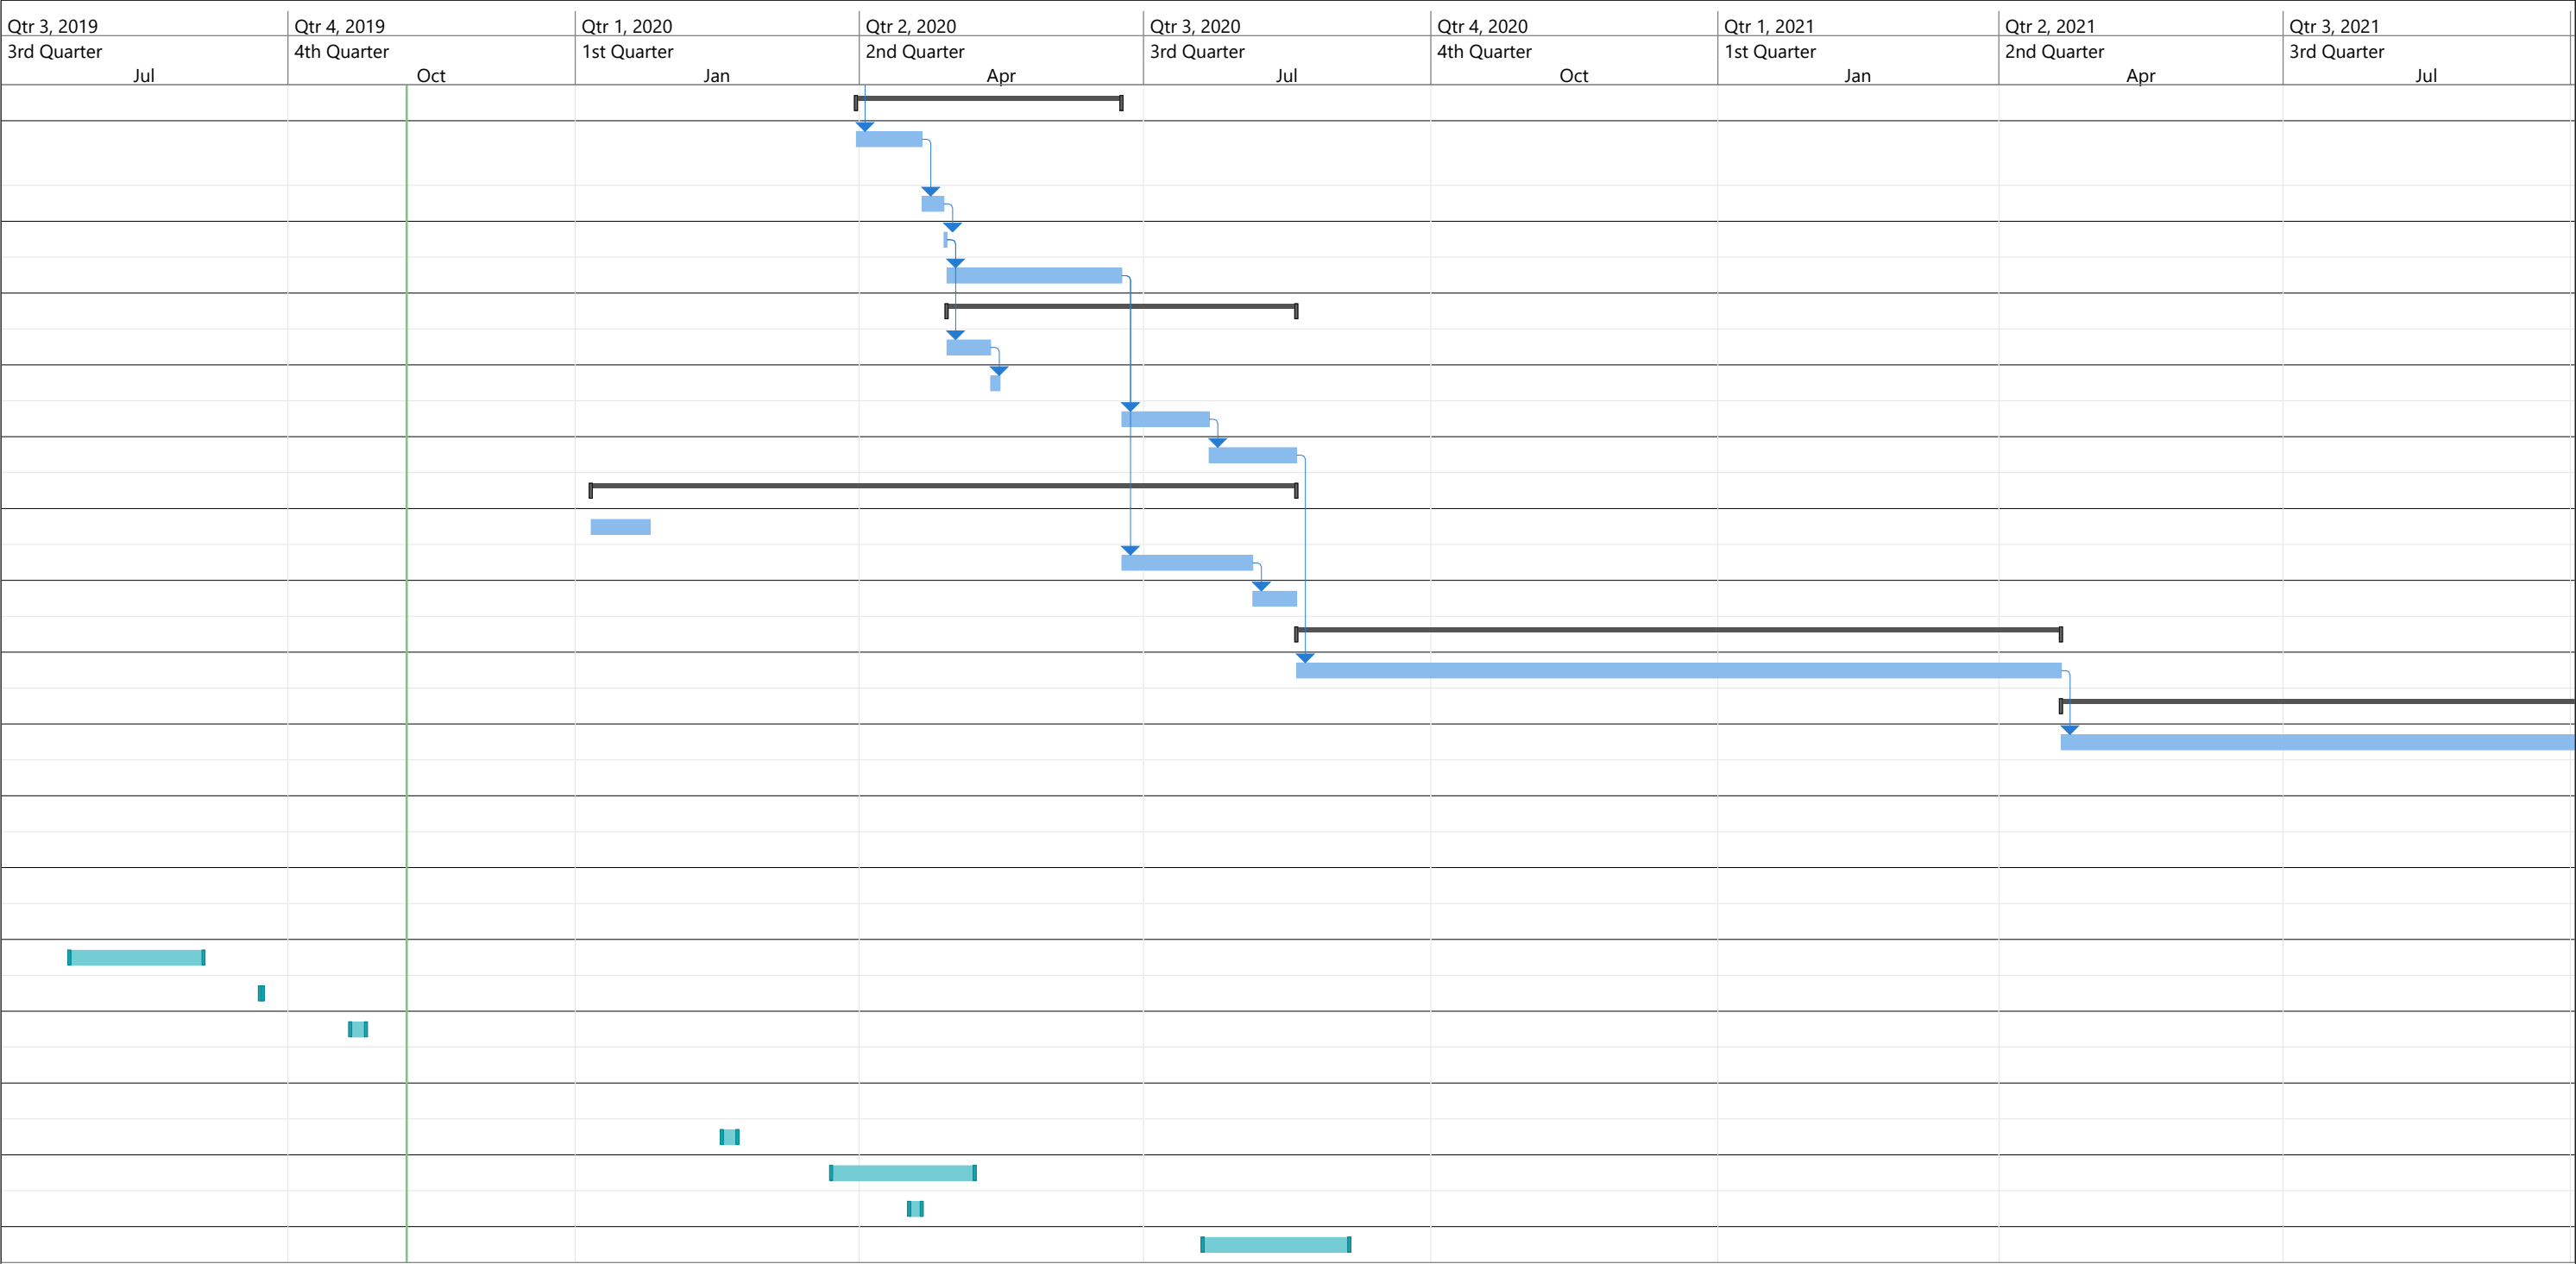


Project: 20181217 LCE Project_P
Date: Fri 08/11/19


Task


Split


Milestone


Summary


 Project Summary


 Inactive Task


 Inactive Milestone


 Inactive Summary


 Manual Task


 Duration-only


 Manual Summary Rollup


 Manual Summary


 Start-only


 Finish-only

 External Tasks

 External Milestone

 Deadline

 Progress

 Manual Progress

